BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Yelahanka Division
Project Name	: "Development of Roads and Drains at Venkatala and Venkatala Janatha Colony in Ward No 01 of Yelahanka Sub Division"
Consultants	: Civil Pro
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 14-Jun-21
Project End Date	: 12-Sep-21
Project Length in Months	: 90 Days

Sl. No	*Assignment*	*Unit*	*Schedule B Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications and directions of the Engineer in charge.	Cum	1698.82	1694.35	100	15-06-21	05-07-21	20
2	Removing and refixing stone slabs of drains and pointing in CM (1:3) complete as per specifications and directions of the Engineer in charge.	Sqm	260.44	219.23	84	16-06-21	27-06-21	11
3	Providing and laying Plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed,	Cum	834.78	834.72	100	20-06-21	14-08-21	55
4	Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal coarse aggregate at 0.69cum and fine aggregate at 0.43cum Machine mixed, well compacted for wall and Bottom including centering shuttering,cost of materials, charge.	Cum	348.37	348.37	100	29-06-21	21-07-21	22

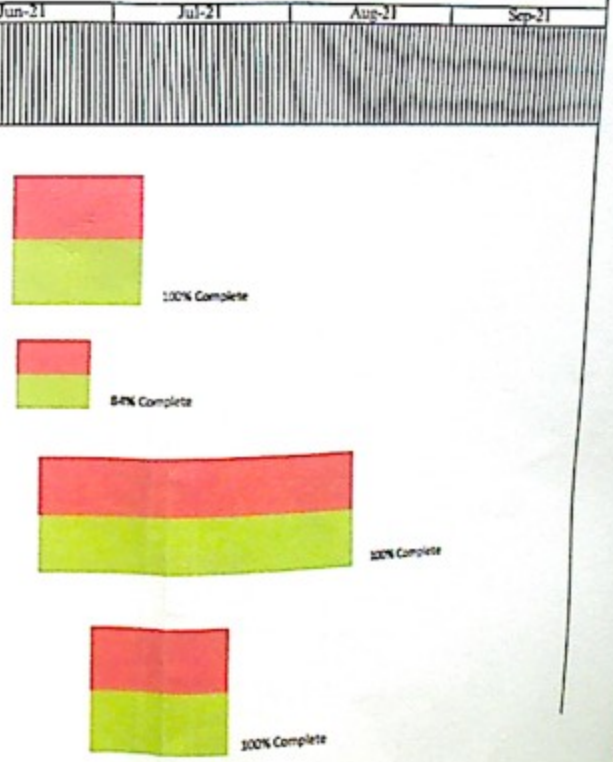

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Yk. Zn)
Yelahanka, Bangalore

...and same may be valid 1 year f... ...Bengaluru, within 21 days of the ... ...Executive Engineer, Yelahanka Divisi... ...Everyday

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	"Development of Roads and Drains at Venkatala and Venkatala Janatha Colony in Ward No 01 of Yelahanka Sub Division"
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	14-Jun-21
Project End Date	:	12-Sep-21
Project Length In Months	:	90 Days

Sl No	*Assignment*	*Unit*	*Schedule B Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
5	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid)	Tonne	23.14	23.14	100	28-06-21	11-07-21	13
6	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,	Sqm	956.50	955.98	100	08-07-21	22-07-21	14
7	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,	Sqm	45.69	45.69	100	10-07-21	25-07-21	15
8	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials,	Cum	21.49	21.49	100	17-07-21	29-07-21	12

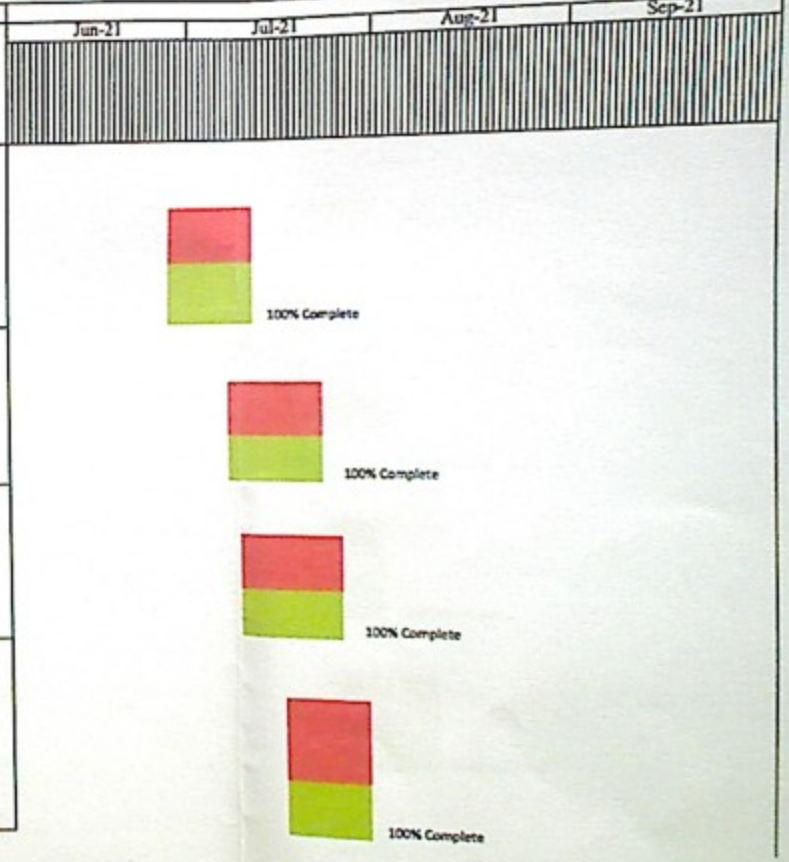

Asst. Executive Engineer
Yelahanka Sub Divison
(BBMP Yng. Zn)
Yelahanka, Bangalore

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	"Development of Roads and Drains at Venkatala and Venkatala Janatha Colony in Ward No 01 of Yelahanka Sub Division"
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	14-Jun-21
Project End Date	:	12-Sep-21
Project Length in Months	:	90 Days

Sl No	*Assignment*	*Unit*	*Schedule B Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
9	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials,	Nos	2388.00	2388.00	100	17-07-21	29-07-21	12
10	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications and directions of the Engineer in charge.	Sqm	429.76	429.76	100	19-07-21	01-08-21	13
11	Scarifying bituminous course 50mm to 75mm thick along with premix carpet / surface dressing by road roller attached with scarifier without disturbing the base and stacking the debris including cost of all labour charges, HOM of machineries	Sqm	761.00	761.00	100	24-07-21	01-08-21	8
12	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and	Cum	1717.92	1692.97	100	25-07-21	09-08-21	15

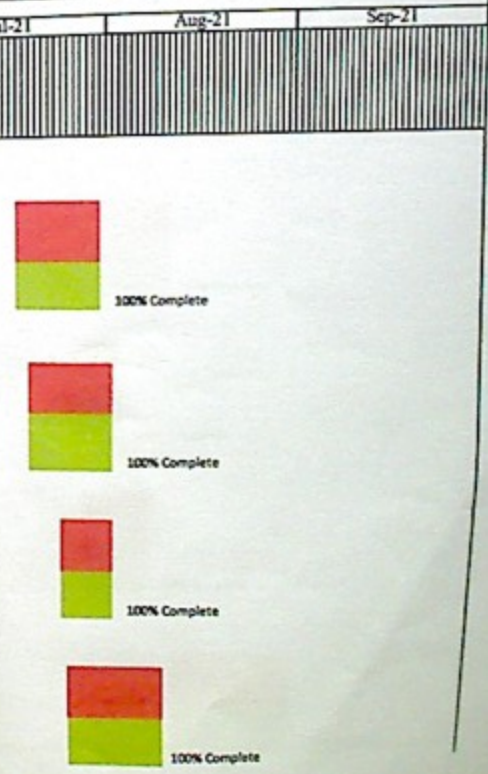

Asst. Executive Engineer
Yelahanka Sub Divison
(BBMP Yrk. Zn)
Yelahanka, Bangalore

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	"Development of Roads and Drains at Venkatala and Venkatala Janatha Colony in Ward No 01 of Yelahanka Sub Division"
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	14-Jun-21
Project End Date	:	12-Sep-21
Project Length in Months	:	90 Days

Sl No	*Assignment*	*Unit*	*Schedule B Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
13	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications and directions of the Engineer in charge.	Sqm	4578.60	4578.60	100	25-07-21	10-08-21	16
14	Construction of Embankment with Material Gravel/ Murrum. KSRRB M300-53. Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site,	Cum	123.40	123.29	100	26-07-21	02-08-21	7
15	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site,	Cum	572.64	572.64	100	28-07-21	07-08-21	10
16	Cement concrete pavement.Construction of un-reinforced plain cement concrete for pavement, using a grade concrete M30 over a prepared base with OPC coarse aggregate @ 0.69cum fine aggregate @ 0.46cum,coarse and fine aggregate confirming to IS:383-2016,	Cum	686.79	686.79	100	12-08-21	30-08-21	18

Asst. Executive Engineer
Yelahanka Sub Divison
(BBMP W.Z. Zn)
Yelahanka, Bangalore
